


EXHIBIT A

ID	Task Name	Duration	Start	Finish	% Complete	Gantt Chart																											
						Jul 15	Jul 29	Aug 12	Aug 26	Sep 9	Sep 23	Oct 7	Oct 21	Nov 4	Nov 18	Dec 2	Dec 16	Dec 30	Jan 13	Jan 27													
1	AL HAVA Project	54.5 days	Wed 7/25/07	Wed 10/10/07	84%	[Gantt bar for AL HAVA Project]																											
2	Requirements	2 days	Wed 7/25/07	Thu 7/26/07	100%	[Gantt bar for Requirements]																											
3	Develop requirements	2 days	Wed 7/25/07	Thu 7/26/07	100%	[Gantt bar for Develop requirements]																											
4	Analysis / approval by Kforce	0 days	Thu 7/26/07	Thu 7/26/07	100%	[Gantt bar for Analysis / approval by Kforce]																											
5	Approval by ES&S	0 days	Thu 7/26/07	Thu 7/26/07	100%	[Gantt bar for Approval by ES&S]																											
6	Approval by customer	0 days	Thu 7/26/07	Thu 7/26/07	100%	[Gantt bar for Approval by customer]																											
7																																	
8	Hardware Procurement and Setup	19.5 days	Wed 7/25/07	Tue 8/21/07	100%	[Gantt bar for Hardware Procurement and Setup]																											
9	Create Server Req	0.5 days	Wed 7/25/07	Wed 7/25/07	100%	[Gantt bar for Create Server Req]																											
10	Purchase 3 Servers	5 days	Wed 7/25/07	Wed 8/1/07	100%	[Gantt bar for Purchase 3 Servers]																											
11	Servers Received	0 days	Wed 8/15/07	Wed 8/15/07	100%	[Gantt bar for Servers Received]																											
12	Setup and configure 3 Servers	2 days	Wed 8/15/07	Fri 8/17/07	100%	[Gantt bar for Setup and configure 3 Servers]																											
13	Verify Server setup/SSL Certificate	2 days	Fri 8/17/07	Tue 8/21/07	100%	[Gantt bar for Verify Server setup/SSL Certificate]																											
14																																	
15	IT Tasks	7 days	Thu 8/30/07	Mon 9/10/07	82%	[Gantt bar for IT Tasks]																											
16	Network configuration to add new Server	2 days	Thu 8/30/07	Fri 8/31/07	100%	[Gantt bar for Network configuration to add new Server]																											
17	Setup Mainframe Access	5 days	Tue 9/4/07	Mon 9/10/07	75%	[Gantt bar for Setup Mainframe Access]																											
18																																	
19	Server SW Development	27.5 days	Fri 7/27/07	Wed 9/5/07	100%	[Gantt bar for Server SW Development]																											
20	Create Web Service Design	1.5 days	Fri 7/27/07	Mon 7/30/07	100%	[Gantt bar for Create Web Service Design]																											
21	Research Web Service Implementation	3 days	Mon 7/30/07	Wed 8/8/07	100%	[Gantt bar for Research Web Service Implementation]																											
22	Design Web Service Interface	2 days	Wed 8/8/07	Fri 8/10/07	100%	[Gantt bar for Design Web Service Interface]																											
23	Server Mainframe I/F coding	10 days	Mon 7/30/07	Fri 8/10/07	100%	[Gantt bar for Server Mainframe I/F coding]																											
24	Write M/F Test Connect App	1.25 days	Mon 7/30/07	Tue 7/31/07	100%	[Gantt bar for Write M/F Test Connect App]																											
25	Write Mainframe simulator	2.5 days	Tue 7/31/07	Thu 8/2/07	100%	[Gantt bar for Write Mainframe simulator]																											
26	Write Mainframe message	6.25 days	Thu 8/2/07	Fri 8/10/07	100%	[Gantt bar for Write Mainframe message]																											
27	Web Service coding	13 days	Fri 8/10/07	Wed 8/29/07	100%	[Gantt bar for Web Service coding]																											
28	Write Web Service Stub	1 day	Fri 8/10/07	Mon 8/13/07	100%	[Gantt bar for Write Web Service Stub]																											
29	Write Ping method	2 days	Mon 8/13/07	Wed 8/15/07	100%	[Gantt bar for Write Ping method]																											
30	Write DPSearch method	2 days	Wed 8/15/07	Fri 8/17/07	100%	[Gantt bar for Write DPSearch method]																											
31	Write AAMVAnetSearch method	2 days	Fri 8/17/07	Tue 8/21/07	100%	[Gantt bar for Write AAMVAnetSearch method]																											
32	Write AAMVAnetResponse method	2 days	Tue 8/21/07	Thu 8/23/07	100%	[Gantt bar for Write AAMVAnetResponse method]																											
33	Get Mailing Address from DMRC DB	2 days	Thu 8/23/07	Mon 8/27/07	100%	[Gantt bar for Get Mailing Address from DMRC DB]																											

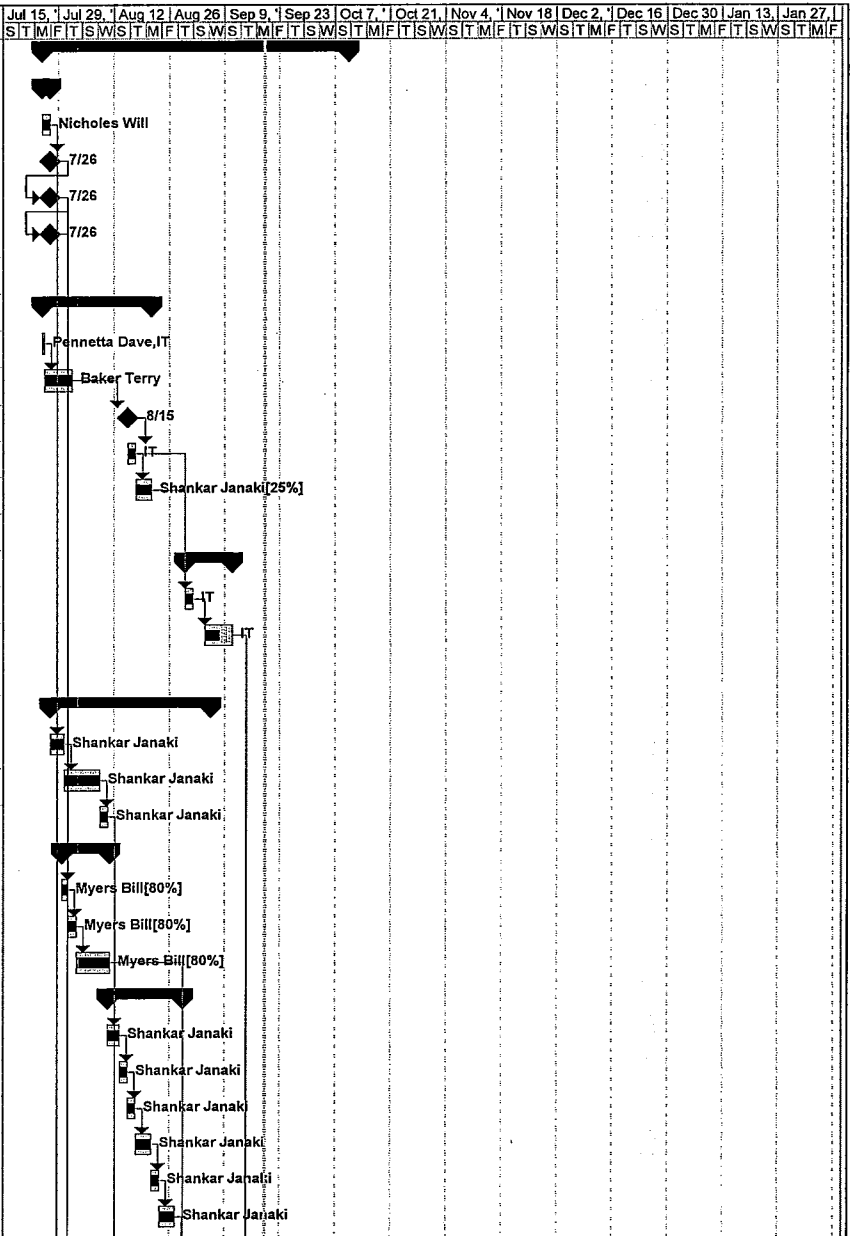

Project: HAVA Draft Schedule
Date: Wed 9/19/07

Task: [Progress bar] Progress
Split: [Milestone diamond] Milestone


Summary: [Summary bar] Summary
Project Summary: [Project Summary bar] Project Summary

External Tasks: [External Task bar] External Tasks
External Milestone: [External Milestone diamond] External Milestone

Deadline: [Deadline arrow] Deadline

Page 1

ID	Task Name	Duration	Start	Finish	% Complete	Jul 15, '07	Jul 29, '07	Aug 12, '07	Aug 26, '07	Sep 9, '07	Sep 23, '07	Oct 7, '07	Oct 21, '07	Nov 4, '07	Nov 18, '07	Dec 2, '07	Dec 16, '07	Dec 30, '07	Jan 13, '08	Jan 27, '08	
34	Unit test web service	2 days	Mon 8/27/07	Wed 8/29/07	100%																
35	Server ES &S I/F coding	10.88 days	Fri 7/27/07	Fri 8/10/07	100%																
36	Write ES &S Simulator - CMD line, C++	10.88 days	Fri 7/27/07	Fri 8/10/07	100%																
37	Integration testing	4 days	Wed 8/29/07	Wed 9/5/07	100%																
38																					
39	Kforce Development	28 days	Fri 7/27/07	Wed 9/5/07	76%																
40	Verify Mainframe Data Access Point	2 days	Fri 7/27/07	Mon 7/30/07	100%																
41	Make database changes	4 days	Fri 7/27/07	Wed 8/1/07	100%																
42	Write program coding	12 days	Thu 8/2/07	Fri 8/17/07	100%																
43	Generate test data	2 days	Thu 8/2/07	Fri 8/3/07	100%																
44	Review Kforce Code	10 days	Thu 8/2/07	Wed 8/15/07	0%																
45	Unit testing of Kforce program	12 days	Mon 8/20/07	Wed 9/5/07	100%																
46																					
47	CM	28.5 days	Fri 7/27/07	Thu 9/6/07	100%																
48	Create BOM	2 days	Fri 7/27/07	Mon 7/30/07	100%																
49	Complete CM Release Engineering tasks	24 days	Tue 7/31/07	Fri 8/31/07	100%																
50	Complete Build Requests	1 day	Wed 9/5/07	Thu 9/6/07	100%																
51																					
52	QA Testing	28 days	Fri 8/10/07	Thu 9/20/07	92%																
53	Test Records	6 days	Thu 8/16/07	Fri 8/24/07	100%																
54	Create test response files for ES&S after DL updat	1.25 days	Wed 9/5/07	Thu 9/6/07	100%																
55	Create Capture Load Test App	6 days	Mon 8/27/07	Tue 9/4/07	100%																
56	Develop test plan	10 days	Fri 8/10/07	Fri 8/24/07	100%																
57	Complete testing - 2 resources	10 days	Thu 9/6/07	Thu 9/20/07	75%																
58																					
59	User Acceptance Testing	17 days	Fri 9/14/07	Tue 10/9/07	20%																
60	Setup UAT test environment	4 days	Fri 9/14/07	Thu 9/20/07	80%																
61	Complete UAT testing - ES&S, Kforce, Digimarc	10 days	Fri 9/21/07	Fri 10/5/07	0%																
62	Approval by customer	2 days	Fri 10/5/07	Tue 10/9/07	0%																
63																					
64	SW Rollout	1 day	Tue 10/9/07	Wed 10/10/07	0%																
65	Mainframe rollout	1 day	Tue 10/9/07	Wed 10/10/07	0%																
66	CS rollout	1 day	Tue 10/9/07	Wed 10/10/07	0%																

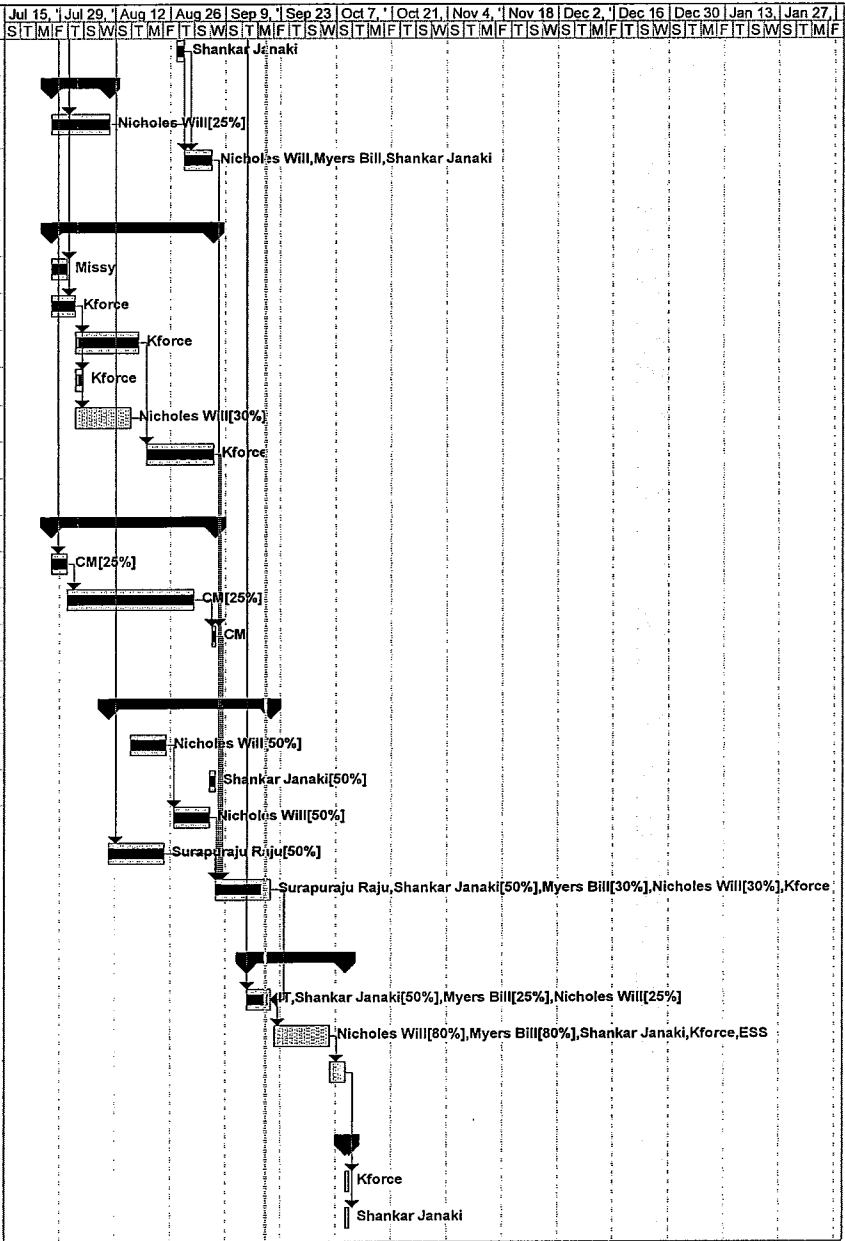

Project: HAVA Draft Schedule
Date: Wed 9/19/07

Task Progress Summary External Tasks Deadline

Split Milestone Project Summary External Milestone
