


EXHIBIT A

Jul 15, Jul 29, Aug 12, Aug 26, Sep 9, Sep 23, Oct 7, Oct 21, Nov 4, Nov 18, Dec 2, Dec 16, Dec 30, Jan 13, Jan 27, Jan 31, Feb 14, Feb 28, Mar 14, Mar 28, Apr 11, Apr 25, May 9, May 23, Jun 6, Jun 20, Jul 4, Jul 18, Aug 1, Aug 15, Aug 29, Sep 12, Sep 26, Oct 10, Oct 24, Nov 7, Nov 21, Dec 5, Dec 19, Dec 31

ID	Task Name	Work	Duration	Start	Finish	% Complete
1	AL HAVA Project	1,505 hrs	54.5 days	Wed 7/25/07	Wed 10/10/07	68%
2	Requirements	16 hrs	2 days	Wed 7/25/07	Thu 7/26/07	100%
3	Develop requirements	16 hrs	2 days	Wed 7/25/07	Thu 7/26/07	100%
4	Analysis / approval by Korce	0 hrs	0 days	Thu 7/26/07	Thu 7/26/07	100%
5	Approval by ES&S	0 hrs	0 days	Thu 7/26/07	Thu 7/26/07	100%
6	Approval by customer	0 hrs	0 days	Thu 7/26/07	Thu 7/26/07	100%
7						
8	Hardware Procurement and Setup	68 hrs	19.5 days	Wed 7/25/07	Tue 8/12/07	100%
9	Create Server Req	8 hrs	0.5 days	Wed 7/25/07	Wed 7/25/07	100%
10	Purchase 3 Servers	40 hrs	5 days	Wed 7/25/07	Wed 8/1/07	100%
11	Servers Received	0 hrs	0 days	Wed 8/15/07	Wed 8/15/07	100%
12	Setup and configure 3 Servers	16 hrs	2 days	Wed 8/15/07	Fri 8/17/07	100%
13	Verify Server setup/SSL Certificate	4 hrs	2 days	Fri 8/17/07	Tue 8/21/07	100%
14						
15	IT Tasks	56 hrs	7 days	Thu 8/30/07	Mon 9/10/07	7%
16	Network configuration to add new Server	16 hrs	2 days	Thu 8/30/07	Fri 8/31/07	25%
17	Setup Mainframe Access	40 hrs	5 days	Tue 9/4/07	Mon 9/10/07	0%
18						
19	Server SW Development	332 hrs	27.5 days	Fri 7/27/07	Wed 9/5/07	97%
20	Create Web Service Design	12 hrs	1.5 days	Fri 7/27/07	Mon 7/30/07	100%
21	Research Web Service Implementation	24 hrs	3 days	Mon 7/30/07	Wed 8/8/07	100%
22	Design Web Service Interface	16 hrs	2 days	Wed 8/8/07	Fri 8/10/07	100%
23	Server Mainframe I/F coding	64 hrs	10 days	Mon 7/30/07	Mon 8/10/07	100%
24	Write M/F Test Connect App	8 hrs	1.25 days	Mon 7/30/07	Tue 7/31/07	100%
25	Write Mainframe simulator	16 hrs	2.5 days	Tue 7/31/07	Tue 8/2/07	100%
26	Write Mainframe message	40 hrs	6.25 days	Thu 8/2/07	Fri 8/10/07	100%
27	Web Service coding	104 hrs	13 days	Fri 8/10/07	Wed 8/29/07	97%
28	Write Web Service Stub	8 hrs	1 day	Fri 8/10/07	Mon 8/13/07	100%
29	Write Ping method	16 hrs	2 days	Mon 8/13/07	Wed 8/15/07	100%
30	Write DPSearch method	16 hrs	2 days	Wed 8/15/07	Fri 8/17/07	90%
31	Write AAMVANAISearch method	16 hrs	2 days	Fri 8/17/07	Tue 8/21/07	100%
32	Write AAMVANAISresponse method	16 hrs	2 days	Tue 8/21/07	Thu 8/23/07	100%
33	Get Mailing Address from DMRC DB	16 hrs	2 days	Thu 8/23/07	Mon 8/27/07	90%

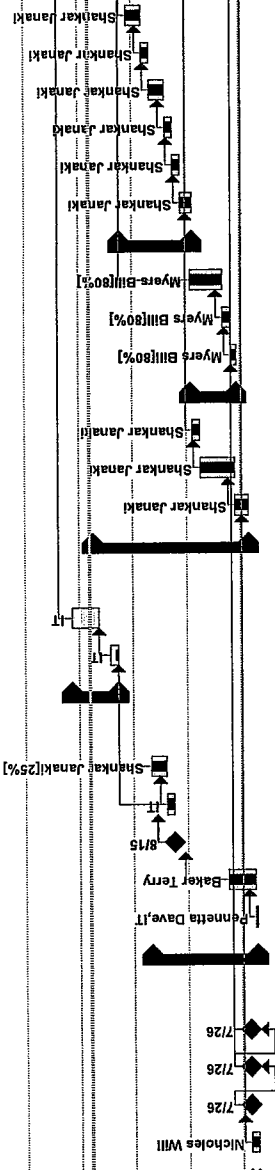


Task Summary Progress Milestone Split

External Tasks External Milestone

Deadline

Project: HAVA Draft Schedule
Date: Thu 9/6/07

ID	Task Name	Work	Duration	Start	Finish	% Complete
34	Unit test web service	16 hrs	2 days	Mon 8/27/07	Wed 8/29/07	100%
35	Server ES & JF coding	16 hrs	10.88 days	Fri 8/10/07	Fri 8/17/07	100%
36	Write ES & S Simulator - CMD line, C++	16 hrs	10.88 days	Fri 7/27/07	Fri 8/10/07	100%
37	Integration testing	96 hrs	4 days	Wed 8/29/07	Wed 9/5/07	75%
38						
39	Kforce Development	280 hrs	28 days	Fri 7/27/07	Wed 9/5/07	74%
40	Verify Manframe Data Access Point	16 hrs	2 days	Fri 7/27/07	Mon 7/30/07	100%
41	Make database changes	32 hrs	4 days	Fri 7/27/07	Wed 8/1/07	100%
42	Write program coding	96 hrs	12 days	Thu 8/2/07	Fri 8/17/07	98%
43	Generate test data	16 hrs	2 days	Thu 8/2/07	Fri 8/3/07	80%
44	Review Kforce Code	24 hrs	10 days	Thu 8/2/07	Wed 8/15/07	0%
45	Unit testing of Kforce program	96 hrs	12 days	Mon 8/20/07	Wed 9/5/07	95%
46						
47	CM	60 hrs	28.5 days	Fri 7/27/07	Thu 9/6/07	100%
48	Create BOM	4 hrs	2 days	Fri 7/27/07	Mon 7/30/07	100%
49	Complete CM Release Engineering tasks	48 hrs	24 days	Tue 7/31/07	Fri 8/31/07	100%
50	Complete Build Requests	8 hrs	1 day	Wed 9/5/07	Thu 9/6/07	100%
51						
52	QA Testing	341 hrs	28 days	Fri 8/10/07	Thu 9/20/07	38%
53	Test Records	24 hrs	6 days	Thu 8/16/07	Fri 8/24/07	67%
54	Create test response files for ESS&S after DL updat	5 hrs	1.25 days	Wed 9/5/07	Thu 9/6/07	0%
55	Create Capture Load Test App	24 hrs	6 days	Mon 8/27/07	Tue 9/4/07	60%
56	Develop test plan	40 hrs	10 days	Fri 8/10/07	Fri 8/24/07	50%
57	Complete testing - 2 resources	248 hrs	10 days	Thu 9/6/07	Thu 9/20/07	0%
58						
59	User Acceptance Testing	336 hrs	17 days	Fri 9/14/07	Tue 10/9/07	0%
60	Setup UAT test environment	64 hrs	4 days	Fri 9/14/07	Thu 9/20/07	0%
61	Complete UAT testing - ESS&S, Kforce, Digmarc	272 hrs	10 days	Fri 9/21/07	Fri 10/5/07	0%
62	Approval by customer	0 hrs	2 days	Fri 10/5/07	Tue 10/9/07	0%
63						
64	SW Rollout	16 hrs	1 day	Tue 10/9/07	Wed 10/10/07	0%
65	Manframe rollout	8 hrs	1 day	Tue 10/9/07	Wed 10/10/07	0%
66	CS rollout	8 hrs	1 day	Tue 10/9/07	Wed 10/10/07	0%

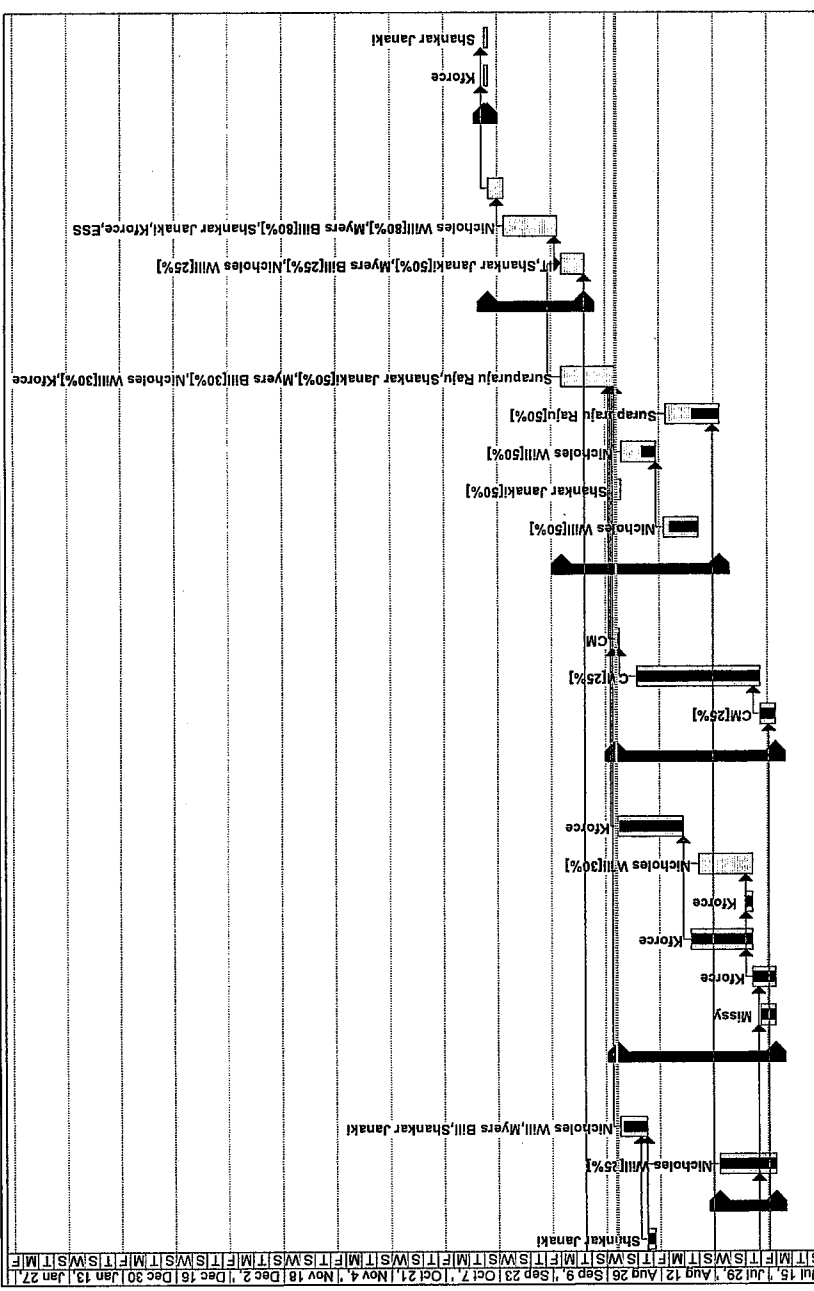

Task Name | Work | Duration | Start | Finish | % Complete
